
Whole garden, house at the bottom

Scale 1:178. Left and right are as seen from the house looking towards the woodland. Grey shapes are existing plants. Coloured dots are the 129 new pots.

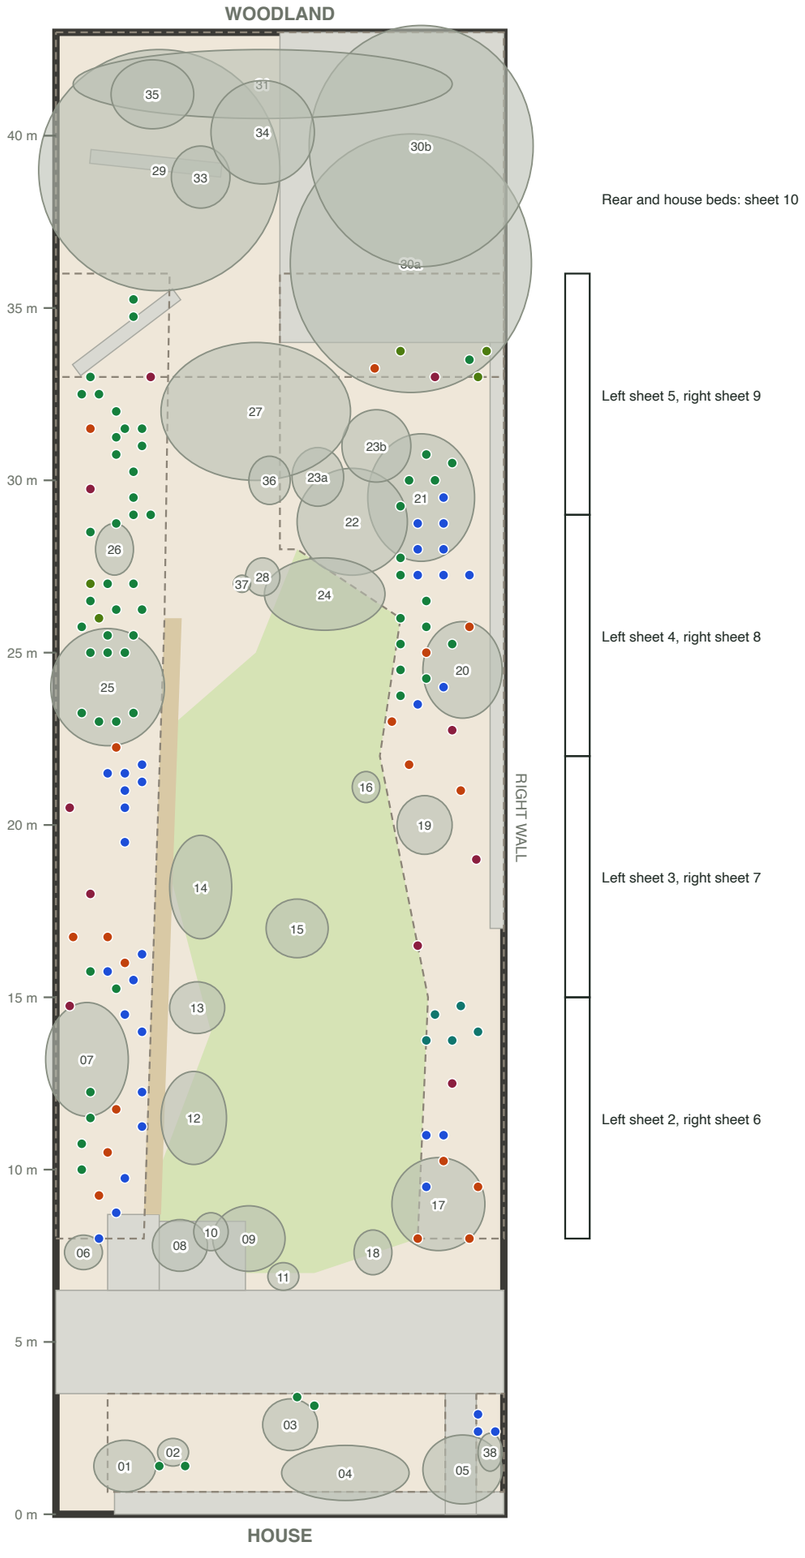

Rear and house beds: sheet 10

Left sheet 5, right sheet 9

Left sheet 4, right sheet 8

Left sheet 3, right sheet 7

Left sheet 2, right sheet 6

NEW PLANTS BY KIND

- Structural shrub: 10 pots
- Flowering shrub: 18 pots
- Perennial: 33 pots
- Grass: 5 pots
- Ground cover: 58 pots
- Fern: 5 pots

EXISTING PLANTS AND FEATURES (grey, numbered as on the survey)

29	Rear-left mature tree / mixed crown
30a	Large right-side tree stem A
30b	Large right-side tree stem B
31	Residual rear vegetation / ivy
01	Golden evergreen, lower bed
02	Cut-back woody shrub
03	Golden clipped evergreen
04	White-variegated lower-bed shrubs
05	Golden evergreen, lower right
06	Small evergreen by left wall
07	Large Elaeagnus-type shrub
08	Golden Euonymus, planter left
09	Golden Euonymus, planter right
10	Mixed flowering / woody planter group
11	Strap-leaved clump by paving
12	Acanthus + strap-leaf group, near
13	Acanthus clump, middle
14	Strap-leaved clump, farther
15	Central Acanthus + woody stems
16	Small sparse shrub in lawn
17	Buddleja by terrace (probable)
18	Small evergreen near terrace
19	Probable Hypericum shrub
20	Right-wall small tree / shrub
21	Tall Buddleja-type shrub
22	Fatsia japonica (probable)
23a	Bamboo, tan / cut-cane clump
23b	Bamboo, dark-caned clump
24	Acanthus groups below Fatsia
25	Left fruit-type tree
26	Heavily cut-back left shrub
27	Low spreading tree, probable apple
28	Small cut-back clump near fruit tree
33	Holly-type shrub, rear understory
34	Orange-fruited rear shrub / small tree
35	Glossy-leaved rear shrub
36	Young Fatsia-type plant by low tree
37	Cut stump in open soil
38	Stair-side bed / rosemary-type shrub

How to use this plan

1. Find the stretch of border on this page and go to its sheet.
2. Hook a tape on the house end of the wall and read the first number along it.
3. Run a second tape straight out from the wall and read the second number.
4. Put the pot down. Set out the whole stretch before digging anything.
5. Where a pot lands on a root, slide it along the bed, not towards the path or lawn.

BEFORE YOU DIG

Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.


Generated 2026-11-05 from the photo survey (rev 04) and the Palmstead order of 129 plants.

Left border, 8 to 15 m from the house

House is to the LEFT of this sheet, woodland to the RIGHT. The LEFT WALL runs along the TOP. Scale 1:25. Dot = pot centre. Faint circle = room the plant needs.

< TOWARDS THE HOUSE

TOWARDS THE WOODLAND >

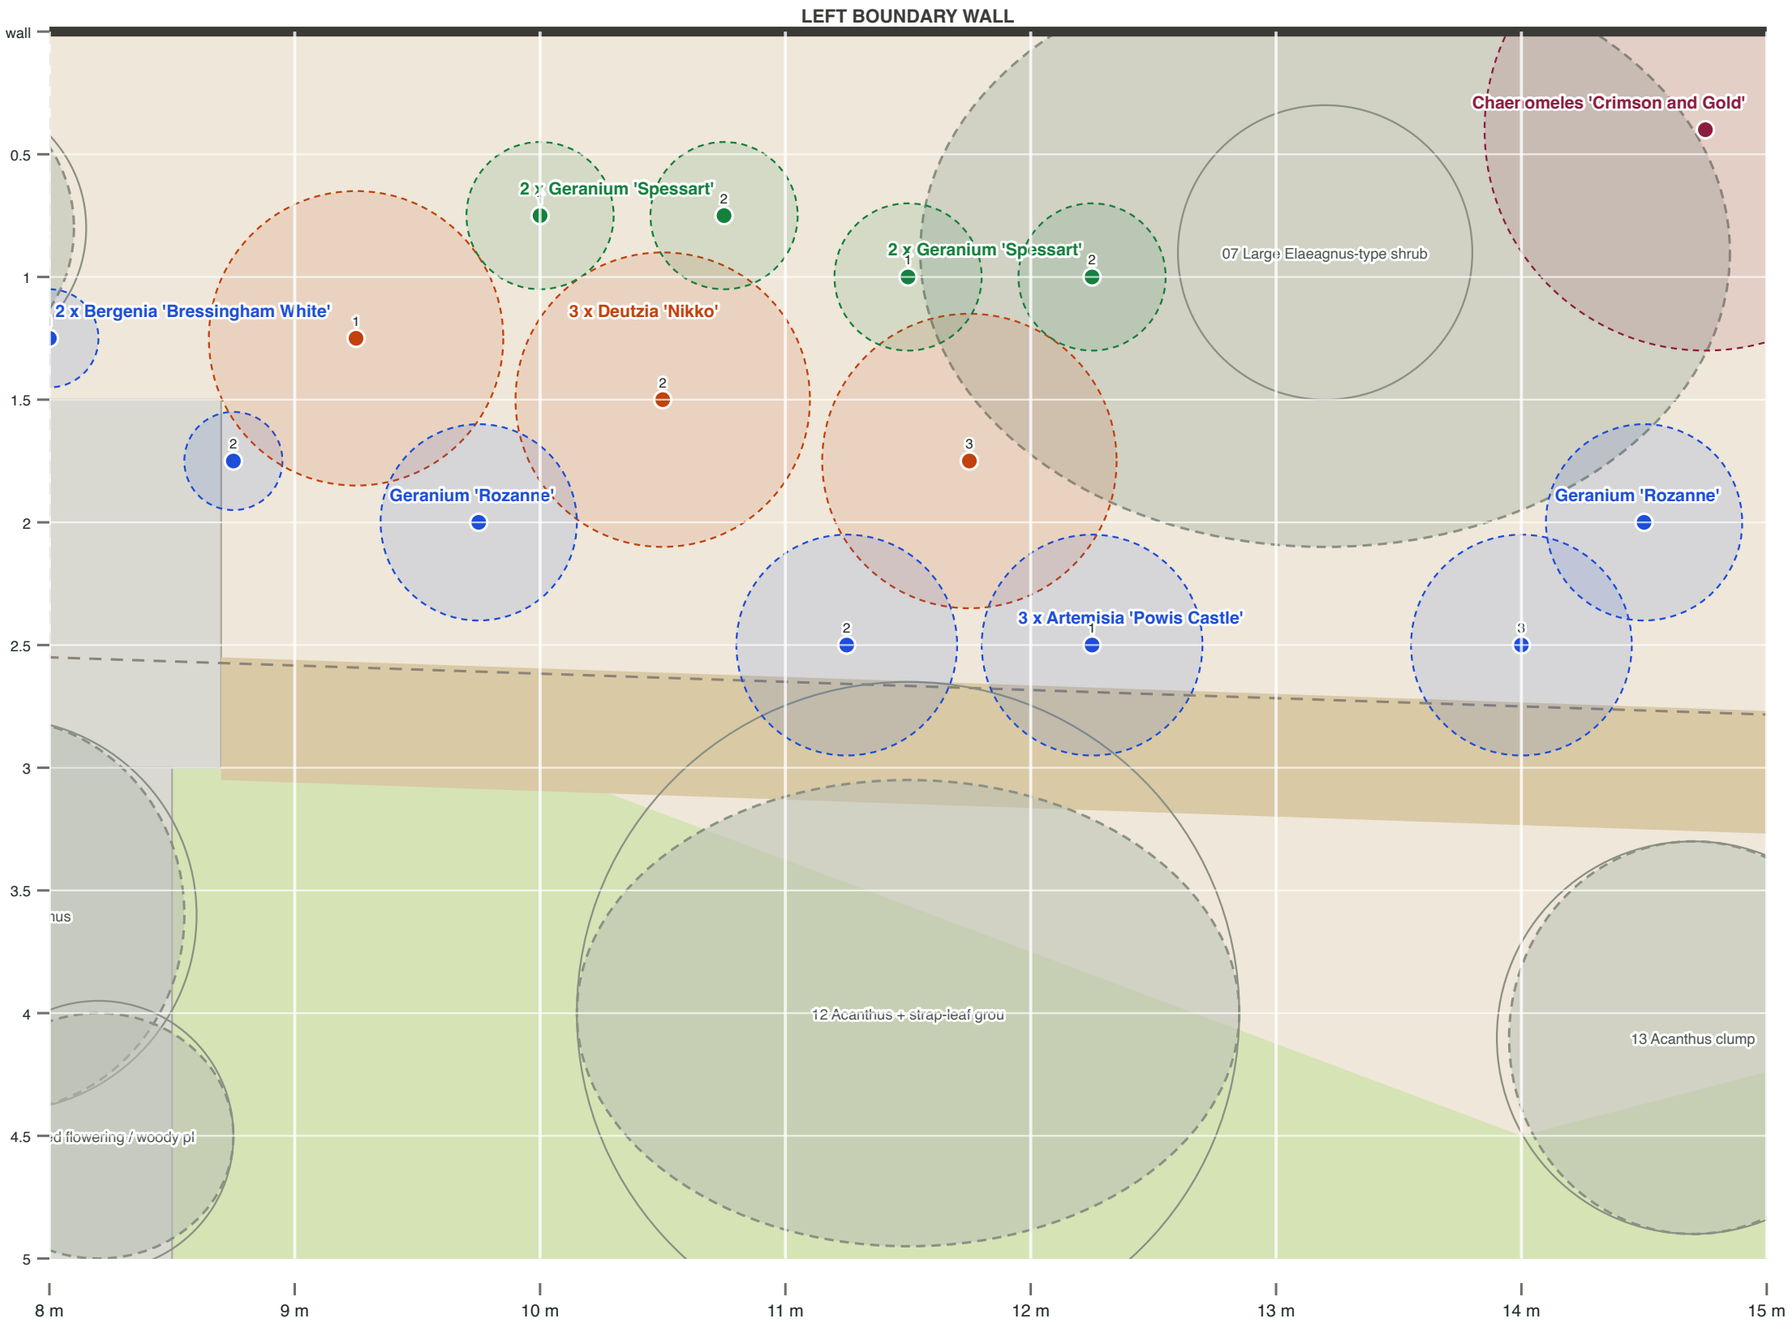

Metres from the house end, measured along the wall

SET OUT: tape along the wall, then out from the wall

- **2 x Bergenia 'Bressingham White'**
  - 1 — 8 along, 1.25 out
  - 2 — 8.75 along, 1.75 out
- **3 x Deutzia 'Nikko'**
  - 1 — 9.25 along, 1.25 out
  - 2 — 10.5 along, 1.5 out
  - 3 — 11.75 along, 1.75 out
- **Geranium 'Rozanne'** — 9.75 along, 2 out
- **2 x Geranium 'Spessart'**
  - 1 — 10 along, 0.75 out
  - 2 — 10.75 along, 0.75 out
- **3 x Artemisia 'Powis Castle'**
  - 1 — 11.25 along, 2.5 out
  - 2 — 12.25 along, 2.5 out
  - 3 — 14 along, 2.5 out
- **2 x Geranium 'Spessart'**
  - 1 — 11.5 along, 1 out
  - 2 — 12.25 along, 1 out
- **Geranium 'Rozanne'** — 14.5 along, 2 out
- **Chaenomeles 'Crimson and Gold'** — 14.75 along, 0.4 out

BEFORE YOU DIG


Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.

Left border, 15 to 22 m from the house

House is to the LEFT of this sheet, woodland to the RIGHT. The LEFT WALL runs along the TOP. Scale 1:25. Dot = pot centre. Faint circle = room the plant needs.

< TOWARDS THE HOUSE

TOWARDS THE WOODLAND >

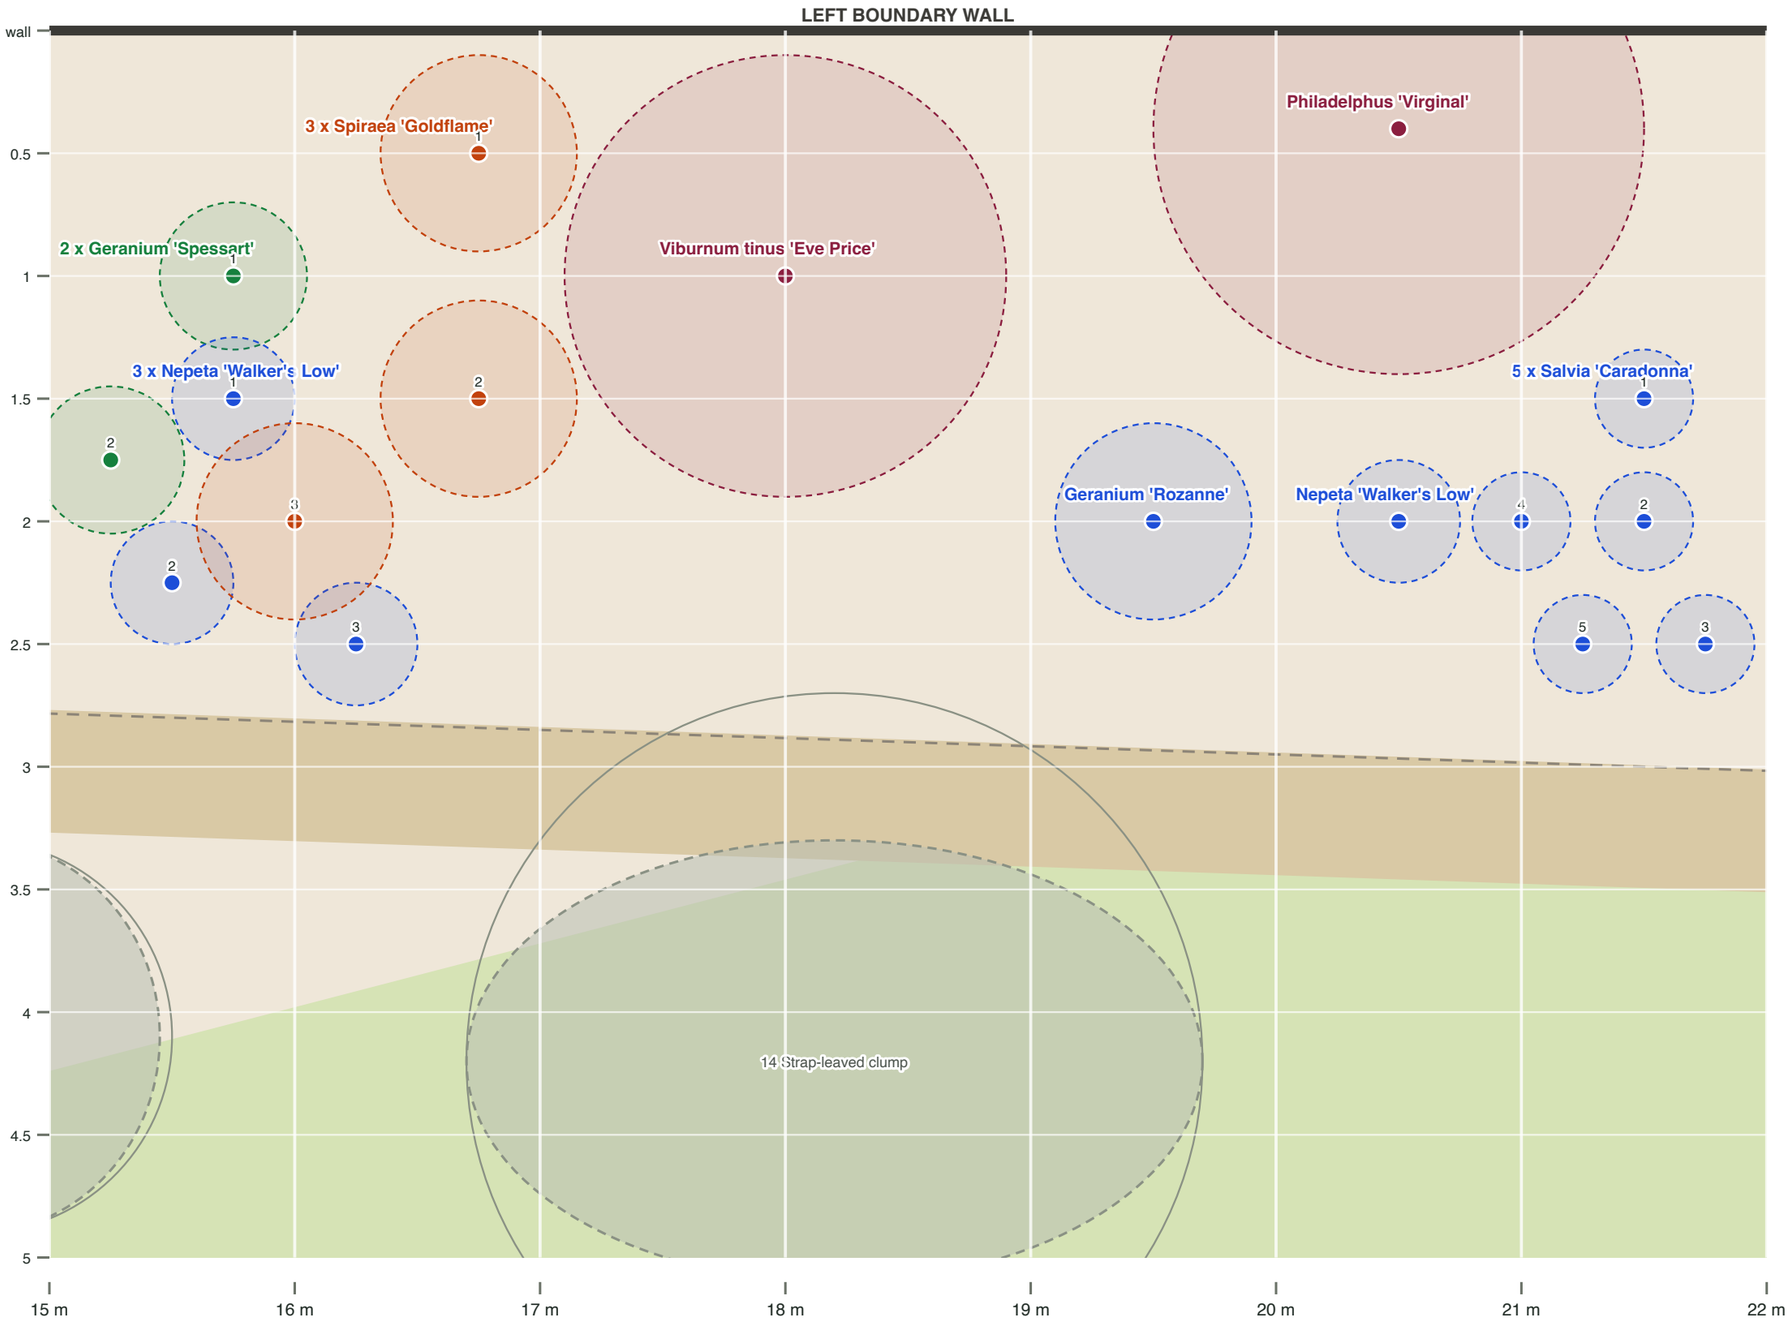

Metres from the house end, measured along the wall

SET OUT: tape along the wall, then out from the wall


2 x Geranium 'Spessart'	
1	15.25 along, 1.75 out
2	15.75 along, 1 out
3 x Nepeta 'Walker's Low'	
1	15.5 along, 2.25 out
2	15.75 along, 1.5 out
3	16.25 along, 2.5 out
3 x Spiraea 'Goldflame'	
1	16 along, 2 out
2	16.75 along, 0.5 out
3	16.75 along, 1.5 out
Viburnum tinus 'Eve Price'	18 along, 1 out
Geranium 'Rozanne'	19.5 along, 2 out
Philadelphus 'Virginal'	20.5 along, 0.4 out
Nepeta 'Walker's Low'	20.5 along, 2 out
5 x Salvia 'Caradonna'	
1	21 along, 2 out
2	21.25 along, 2.5 out
3	21.5 along, 1.5 out
4	21.5 along, 2 out
5	21.75 along, 2.5 out

BEFORE YOU DIG

Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.

Left border, 22 to 29 m from the house

House is to the LEFT of this sheet, woodland to the RIGHT. The LEFT WALL runs along the TOP. Scale 1:25. Dot = pot centre. Faint circle = room the plant needs.

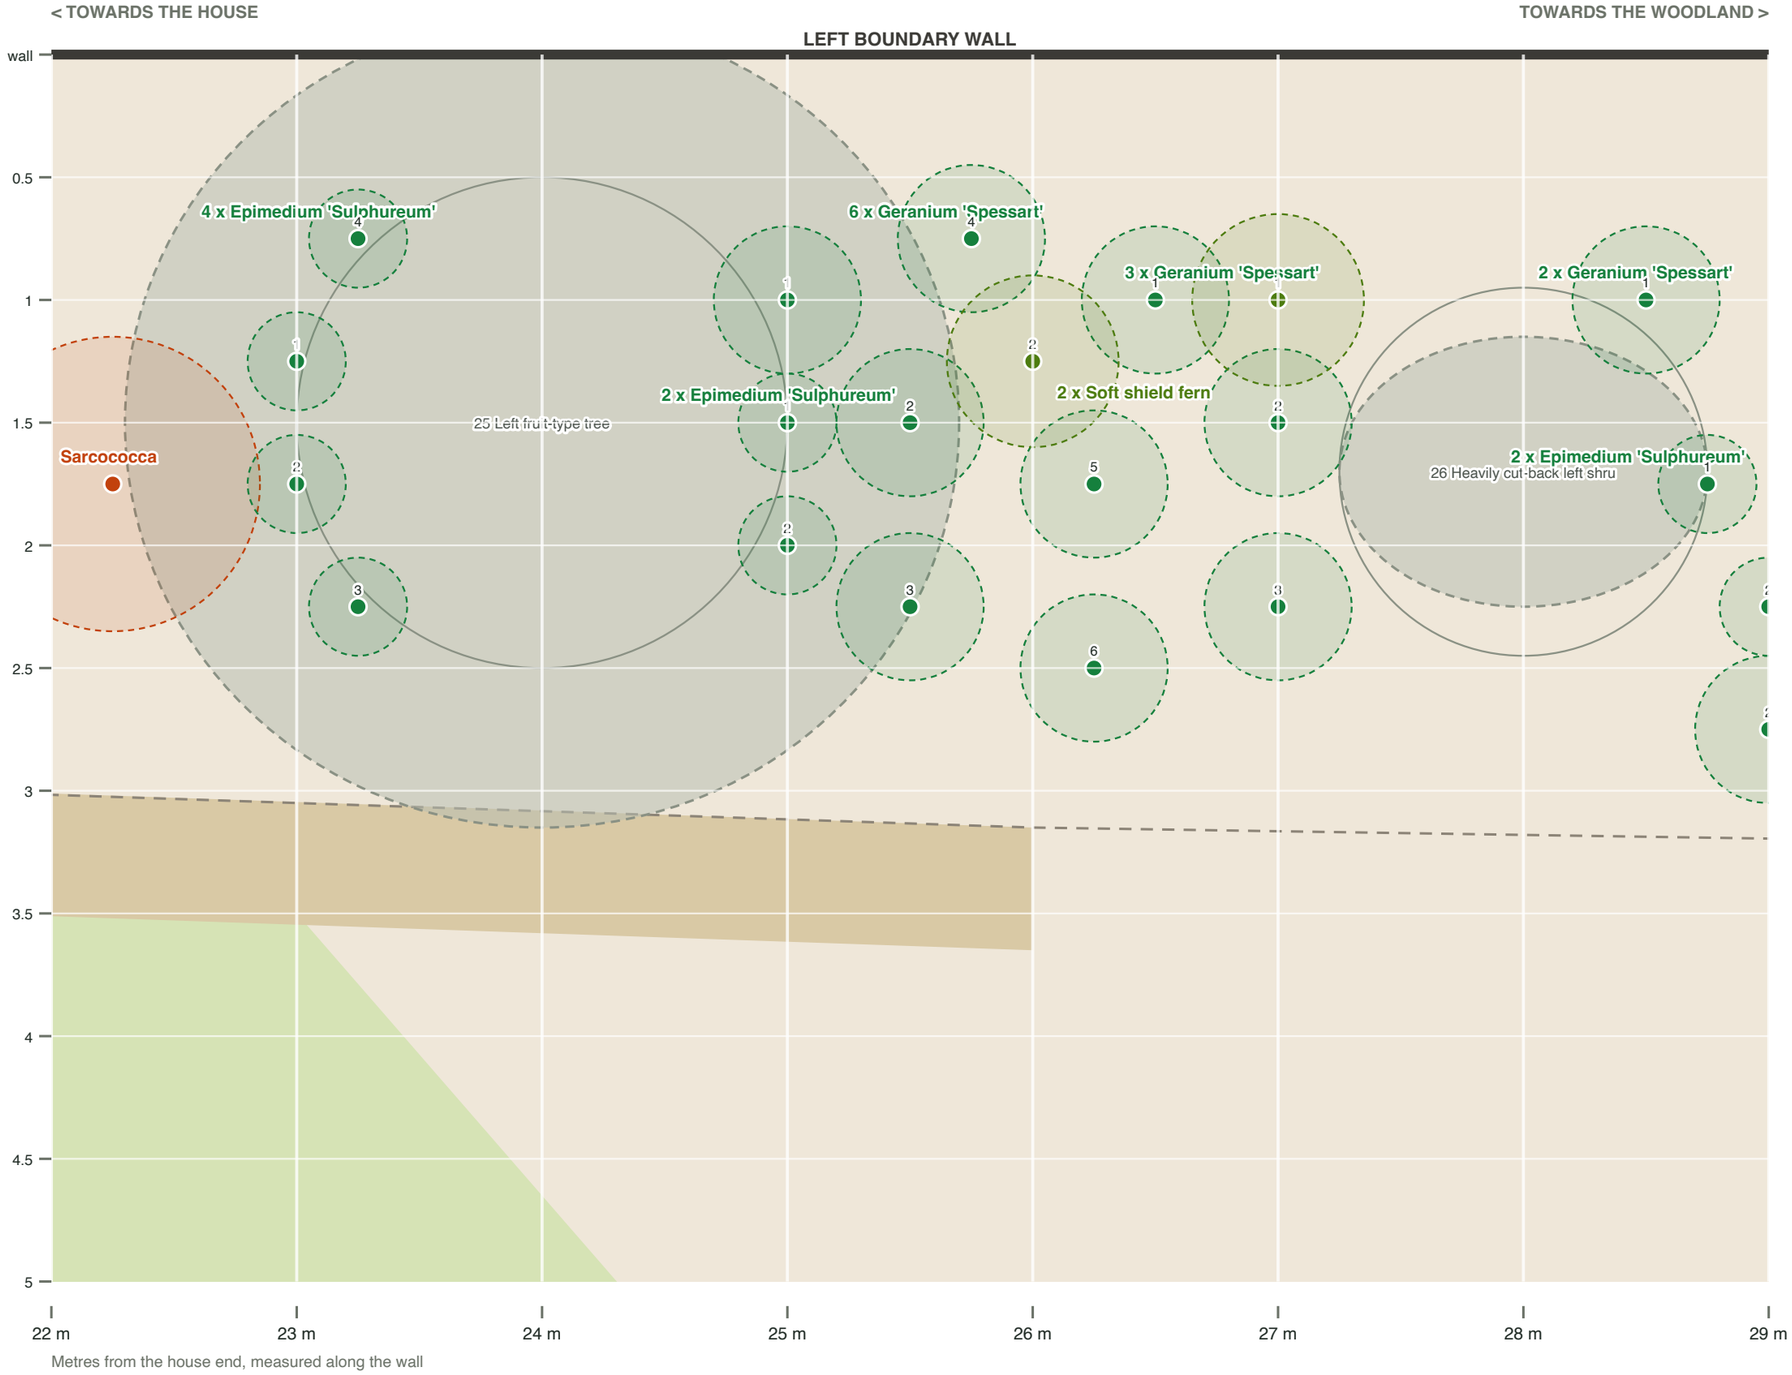

SET OUT: tape along the wall, then out from the wall

Sarcococca	22.25 along, 1.75 out
4 x Epimedium 'Sulphureum'	
1	23 along, 1.25 out
2	23 along, 1.75 out
3	23.25 along, 0.75 out
4	23.25 along, 2.25 out
6 x Geranium 'Spessart'	
1	25 along, 1 out
2	25.5 along, 1.5 out
3	25.5 along, 2.25 out
4	25.75 along, 0.75 out
5	26.25 along, 1.75 out
6	26.25 along, 2.5 out
2 x Epimedium 'Sulphureum'	
1	25 along, 1.5 out
2	25 along, 2 out
2 x Soft shield fern	
1	26 along, 1.25 out
2	27 along, 1 out
3 x Geranium 'Spessart'	
1	26.5 along, 1 out
2	27 along, 1.5 out
3	27 along, 2.25 out
2 x Geranium 'Spessart'	
1	28.5 along, 1 out
2	29 along, 2.75 out
2 x Epimedium 'Sulphureum'	
1	28.75 along, 1.75 out
2	29 along, 2.25 out

BEFORE YOU DIG


Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.

Left border, 29 to 36 m from the house

House is to the LEFT of this sheet, woodland to the RIGHT. The LEFT WALL runs along the TOP. Scale 1:25. Dot = pot centre. Faint circle = room the plant needs.

< TOWARDS THE HOUSE

TOWARDS THE WOODLAND >

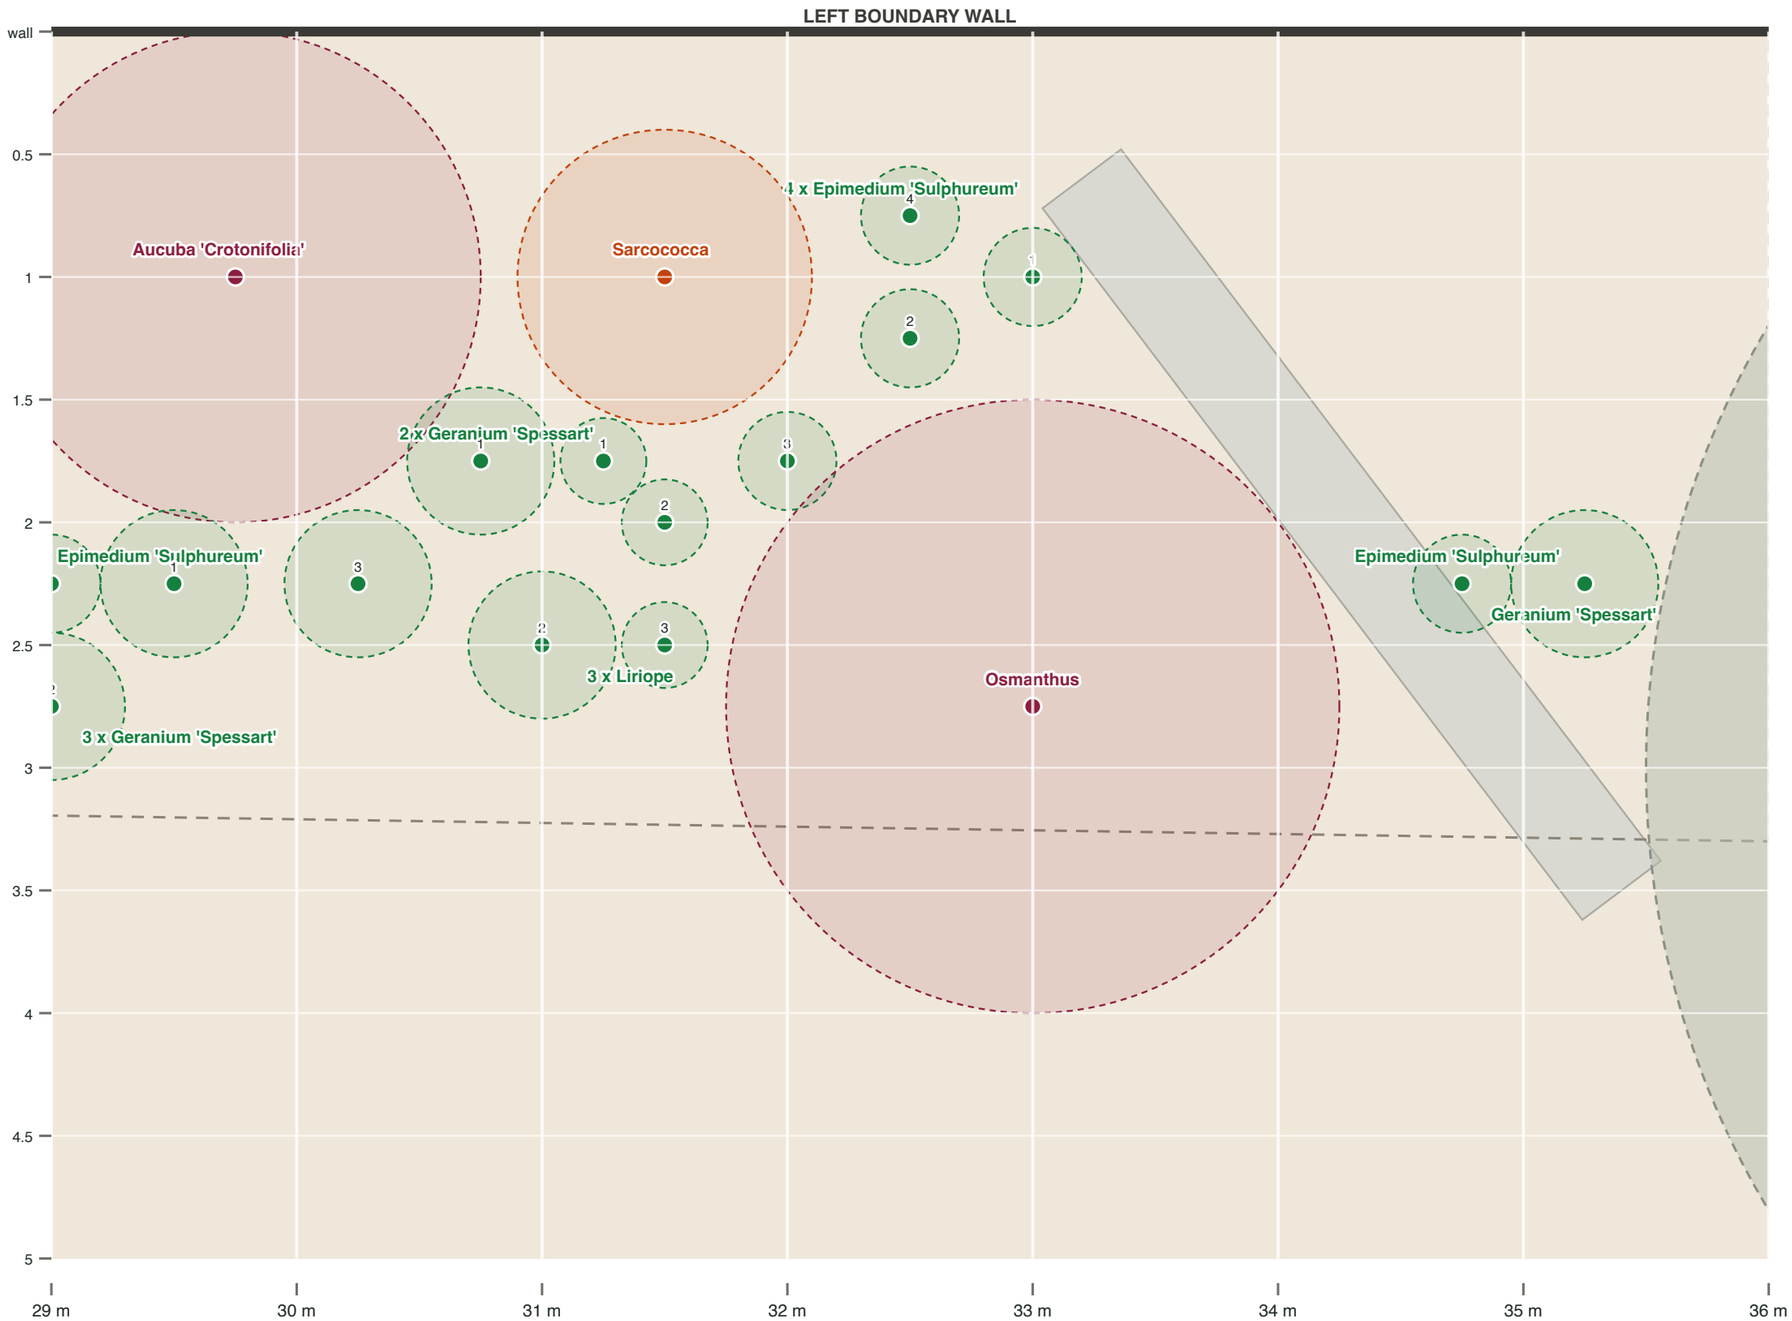

SET OUT: tape along the wall, then out from the wall

Epimedium 'Sulphureum'	29 along, 2.25 out
3 x Geranium 'Spessart'	
1	29 along, 2.75 out
2	29.5 along, 2.25 out
3	30.25 along, 2.25 out
Aucuba 'Crotonifolia'	29.75 along, 1 out
2 x Geranium 'Spessart'	
1	30.75 along, 1.75 out
2	31 along, 2.5 out
3 x Liriope	
1	31.25 along, 1.75 out
2	31.5 along, 2 out
3	31.5 along, 2.5 out
Sarcococca	31.5 along, 1 out
4 x Epimedium 'Sulphureum'	
1	32 along, 1.75 out
2	32.5 along, 0.75 out
3	32.5 along, 1.25 out
4	33 along, 1 out
Osmanthus	33 along, 2.75 out
Epimedium 'Sulphureum'	34.75 along, 2.25 out
Geranium 'Spessart'	35.25 along, 2.25 out

BEFORE YOU DIG


Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.

Right border, 8 to 15 m from the house

House is to the LEFT of this sheet, woodland to the RIGHT. The RIGHT WALL runs along the BOTTOM. Scale 1:25. Dot = pot centre. Faint circle = room the plant needs.

< TOWARDS THE HOUSE

TOWARDS THE WOODLAND >

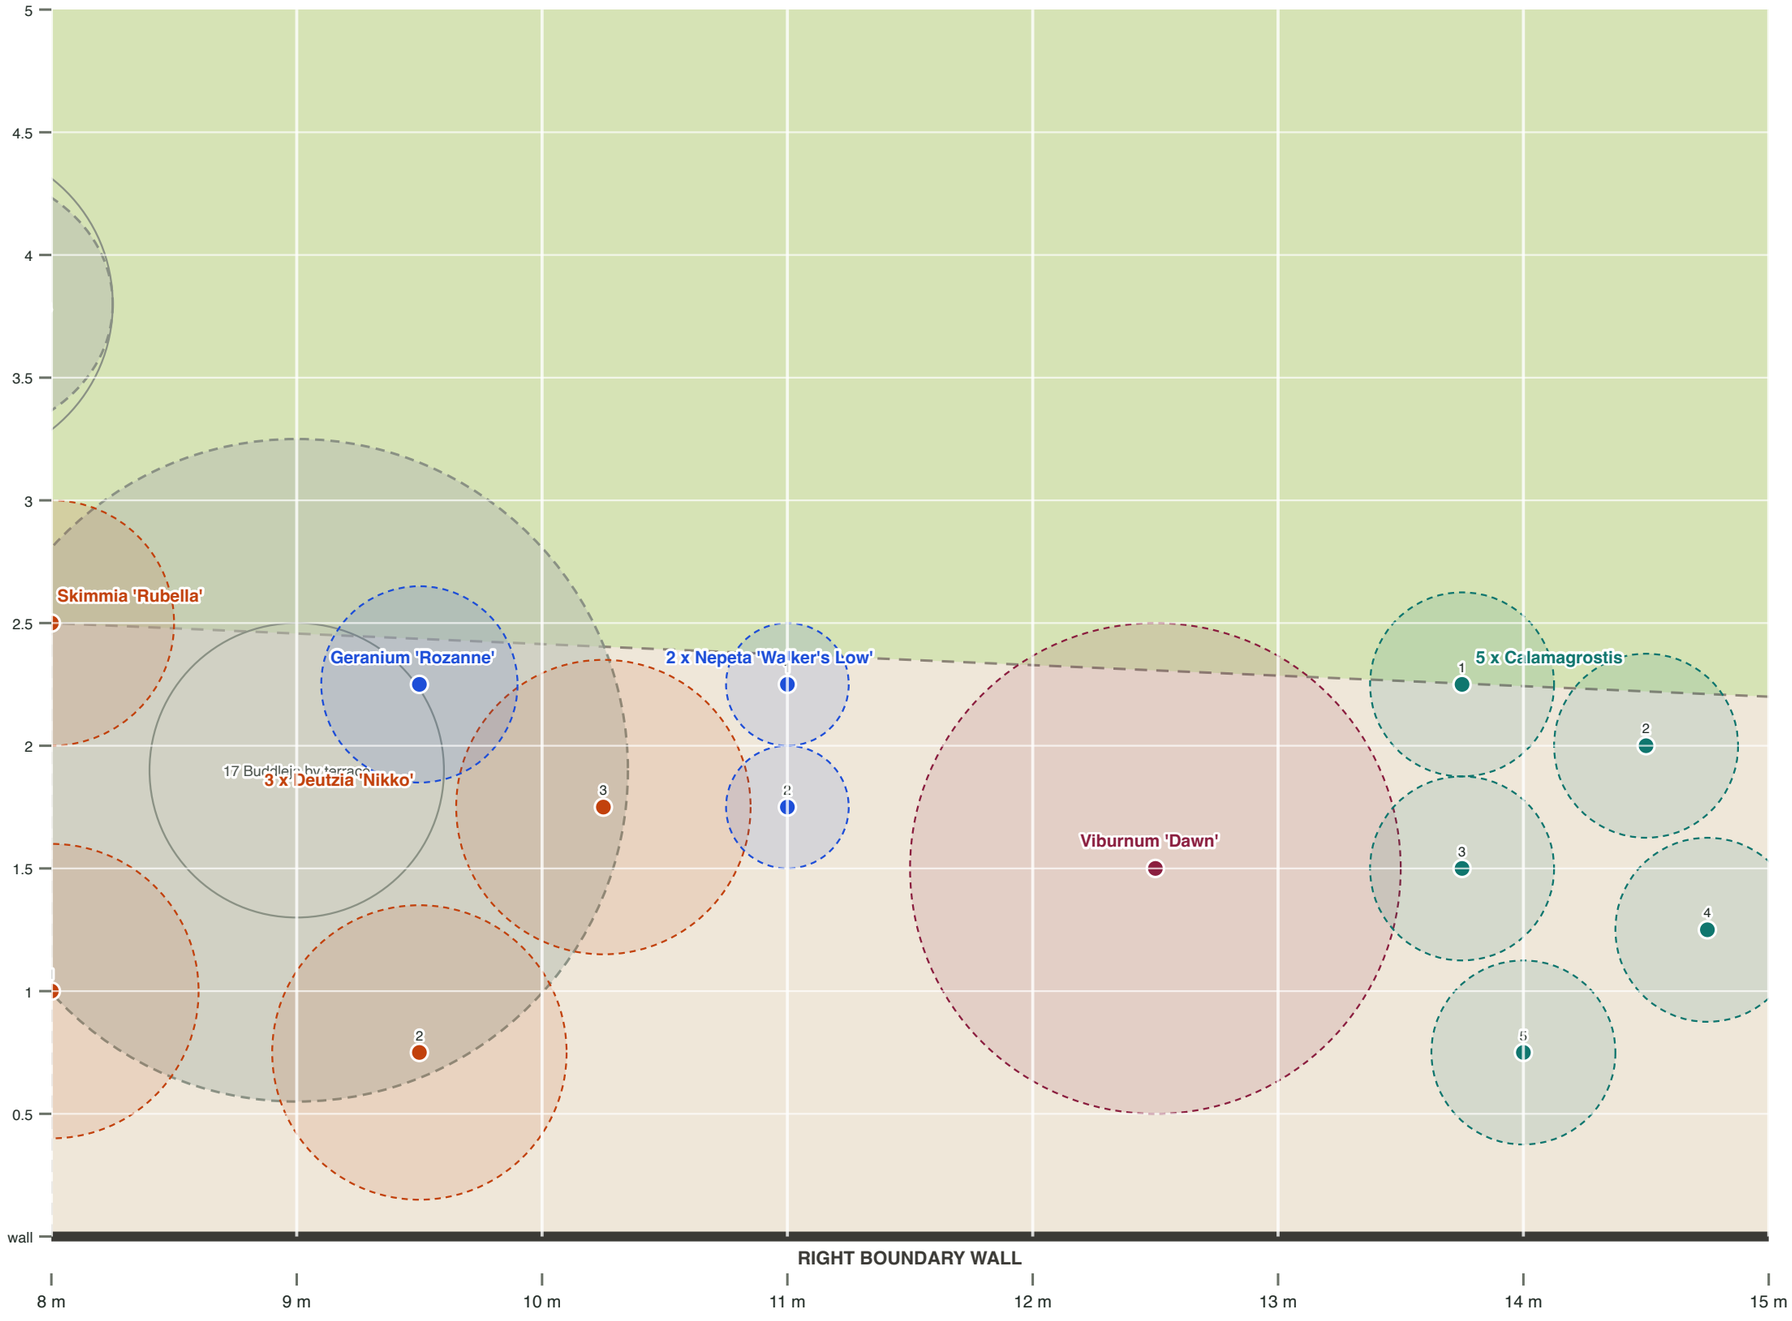

Metres from the house end, measured along the wall

SET OUT: tape along the wall, then out from the wall

Skimmia 'Rubella'	8 along, 2.5 out
3 x Deutzia 'Nikko'	
1	8 along, 1 out
2	9.5 along, 0.75 out
3	10.25 along, 1.75 out
Geranium 'Rozanne'	9.5 along, 2.25 out
2 x Nepeta 'Walker's Low'	
1	11 along, 2.25 out
2	11 along, 1.75 out
Viburnum 'Dawn'	12.5 along, 1.5 out
5 x Calamagrostis	
1	13.75 along, 2.25 out
2	13.75 along, 1.5 out
3	14 along, 0.75 out
4	14.5 along, 2 out
5	14.75 along, 1.25 out

BEFORE YOU DIG


Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.

Right border, 15 to 22 m from the house

House is to the LEFT of this sheet, woodland to the RIGHT. The RIGHT WALL runs along the BOTTOM. Scale 1:25. Dot = pot centre. Faint circle = room the plant needs.

< TOWARDS THE HOUSE

TOWARDS THE WOODLAND >

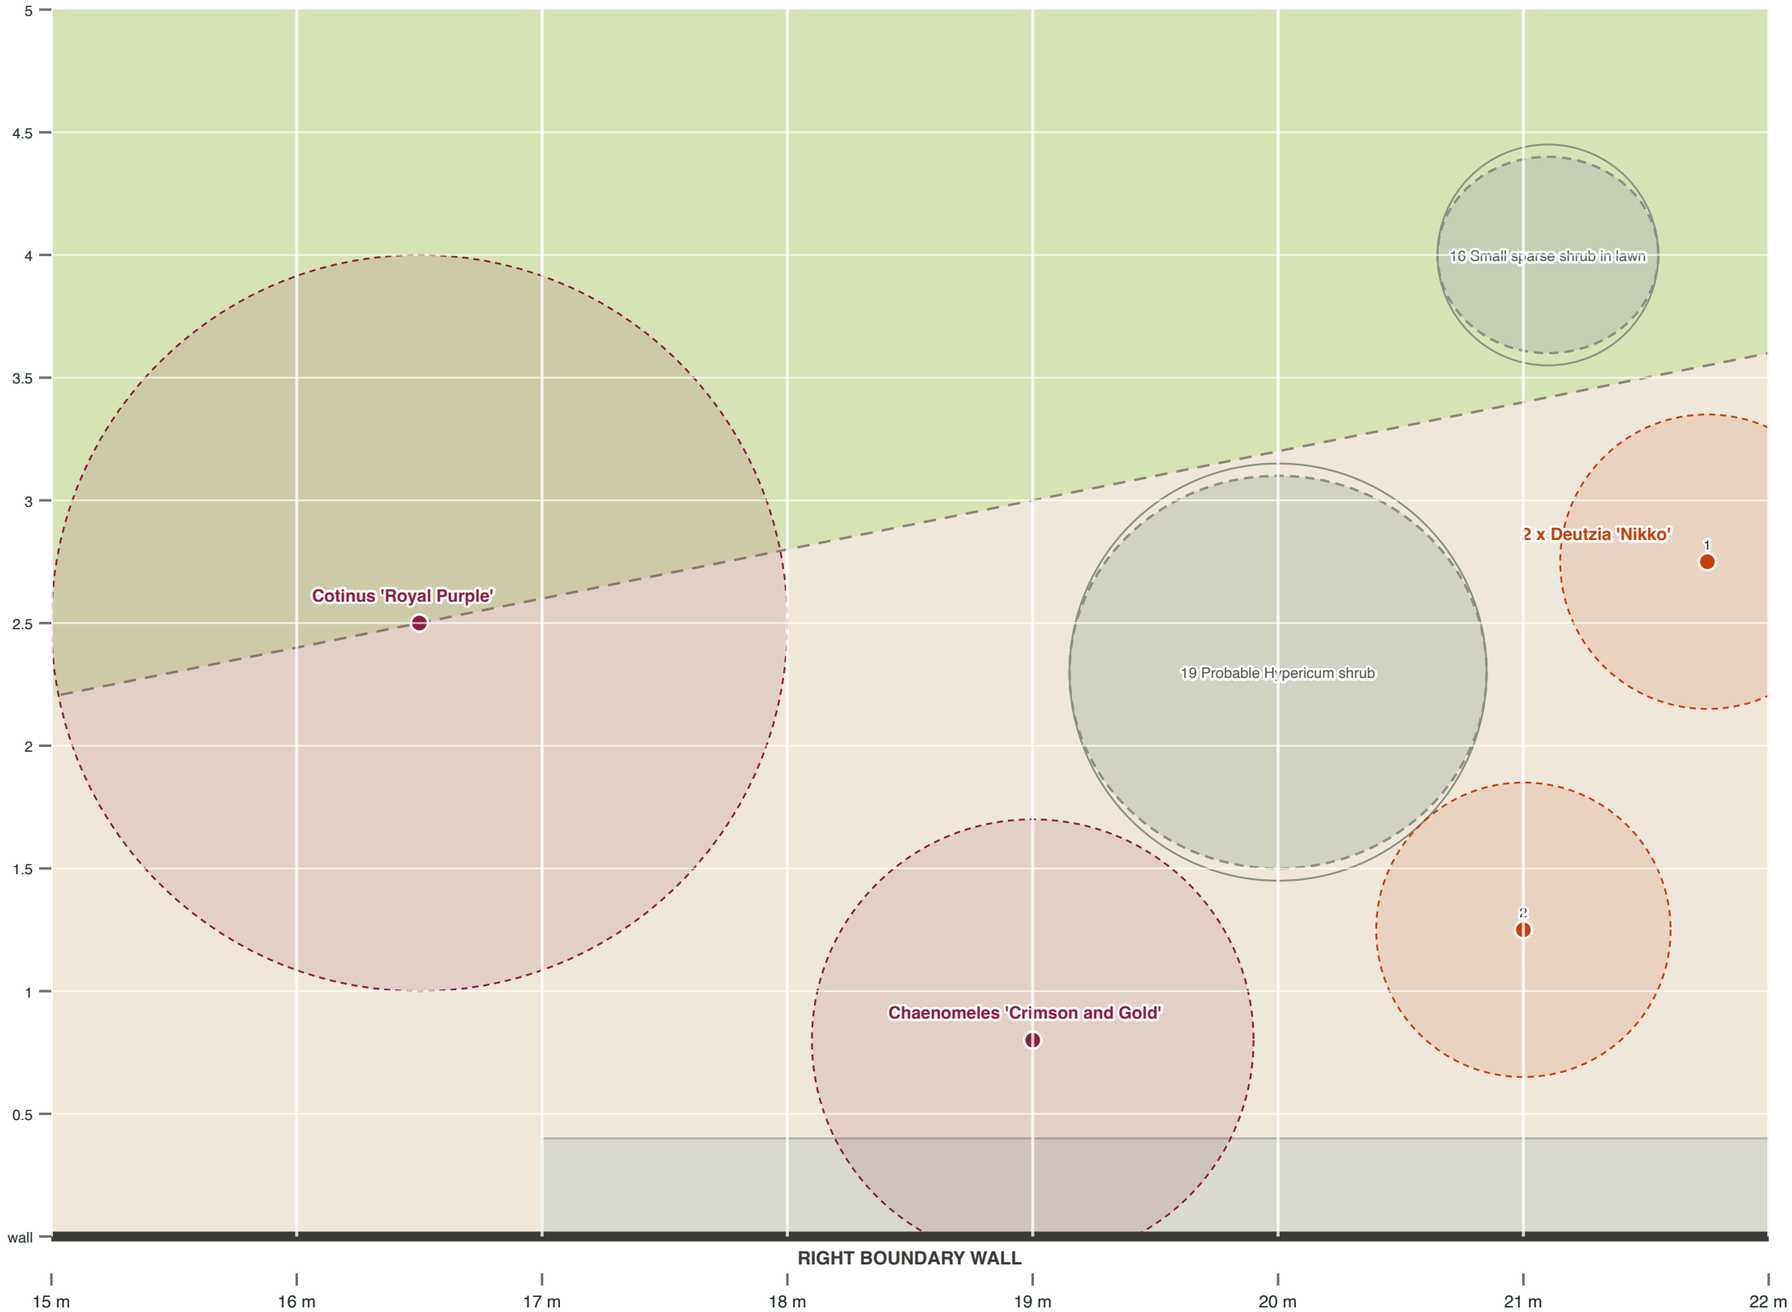

SET OUT: tape along the wall, then out from the wall

Cotinus 'Royal Purple'	16.5 along, 2.5 out
Chaenomeles 'Crimson and Gold'	19 along, 0.8 out
2 x Deutzia 'Nikko'	
1	21 along, 1.25 out
2	21.75 along, 2.75 out

BEFORE YOU DIG

Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.


Generated 2026-11-05 from the photo survey (rev 04) and the Palmstead order of 129 plants.

Right border, 22 to 29 m from the house

House is to the LEFT of this sheet, woodland to the RIGHT. The RIGHT WALL runs along the BOTTOM. Scale 1:25. Dot = pot centre. Faint circle = room the plant needs.

< TOWARDS THE HOUSE

TOWARDS THE WOODLAND >

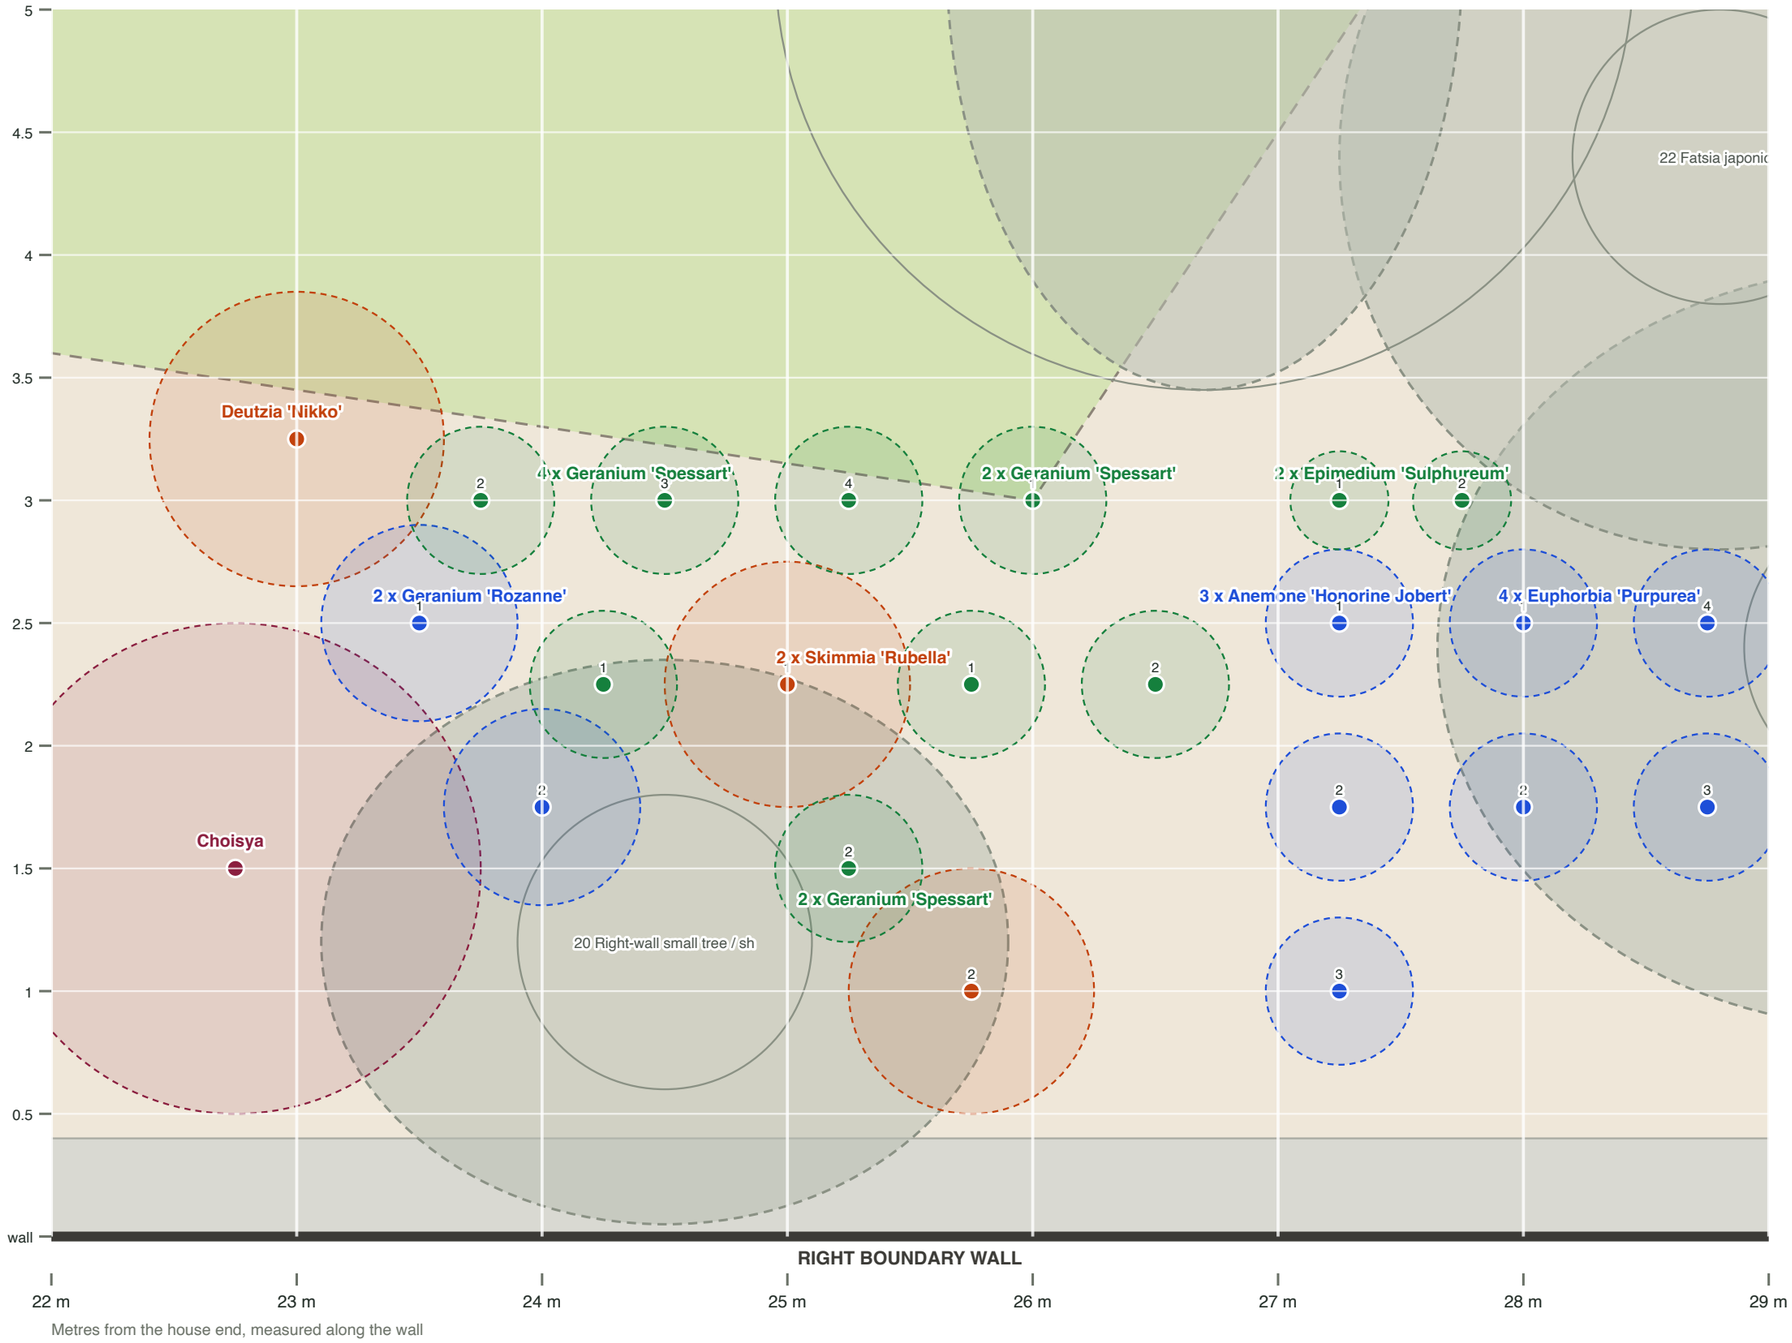

SET OUT: tape along the wall, then out from the wall

Choisya	22.75 along, 1.5 out
Deutzia 'Nikko'	23 along, 3.25 out
2 x Geranium 'Rozanne'	
1	23.5 along, 2.5 out
2	24 along, 1.75 out
4 x Geranium 'Spessart'	
1	23.75 along, 3 out
2	24.25 along, 2.25 out
3	24.5 along, 3 out
4	25.25 along, 3 out
2 x Skimmia 'Rubella'	
1	25 along, 2.25 out
2	25.75 along, 1 out
2 x Geranium 'Spessart'	
1	25.25 along, 1.5 out
2	25.75 along, 2.25 out
2 x Geranium 'Spessart'	
1	26 along, 3 out
2	26.5 along, 2.25 out
2 x Epimedium 'Sulphureum'	
1	27.25 along, 3 out
2	27.75 along, 3 out
3 x Anemone 'Honorine Jobert'	
1	27.25 along, 2.5 out
2	27.25 along, 1.75 out
3	27.25 along, 1 out
4 x Euphorbia 'Purpurea'	
1	28 along, 2.5 out
2	28 along, 1.75 out
3	28.75 along, 2.5 out
4	28.75 along, 1.75 out

BEFORE YOU DIG


Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.

Right border, 29 to 36 m from the house

House is to the LEFT of this sheet, woodland to the RIGHT. The RIGHT WALL runs along the BOTTOM. Scale 1:25. Dot = pot centre. Faint circle = room the plant needs.

< TOWARDS THE HOUSE

TOWARDS THE WOODLAND >

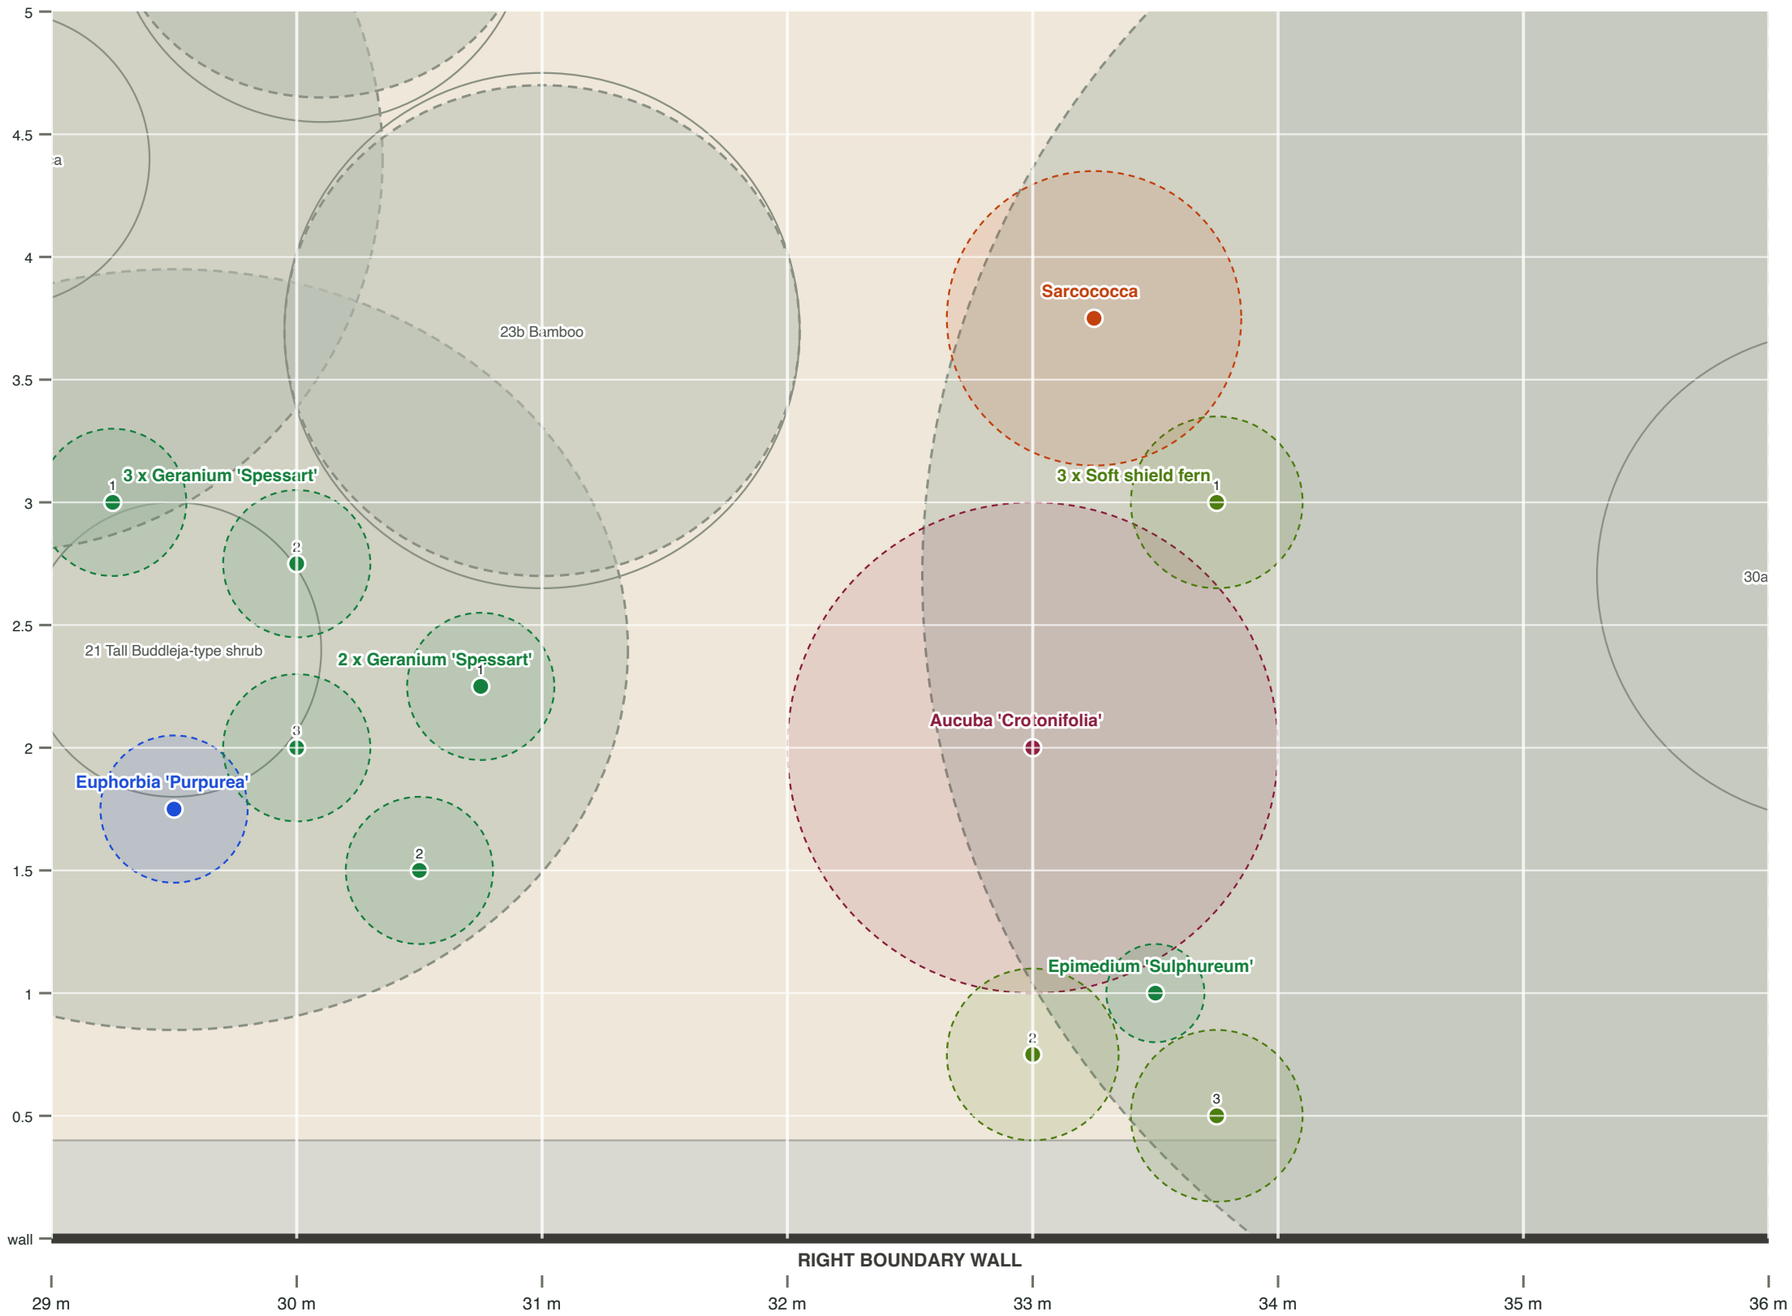

SET OUT: tape along the wall, then out from the wall

3 x Geranium 'Spessart'	
1	29.25 along, 3 out
2	30 along, 2.75 out
3	30 along, 2 out
Euphorbia 'Purpurea'	29.5 along, 1.75 out
2 x Geranium 'Spessart'	
1	30.5 along, 1.5 out
2	30.75 along, 2.25 out
Aucuba 'Crotonifolia'	33 along, 2 out
3 x Soft shield fern	
1	33 along, 0.75 out
2	33.75 along, 3 out
3	33.75 along, 0.5 out
Sarcococca	33.25 along, 3.75 out
Epimedium 'Sulphureum'	33.5 along, 1 out


BEFORE YOU DIG

Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.


Rear woodland and house beds

Scale 1:68. House at the bottom of each panel. The lawn and borders between 3.5 m and 31 m are on sheets 2 to 9.

REAR WOODLAND, the last 12 m before the rear wall (31 to 43 m from the house)

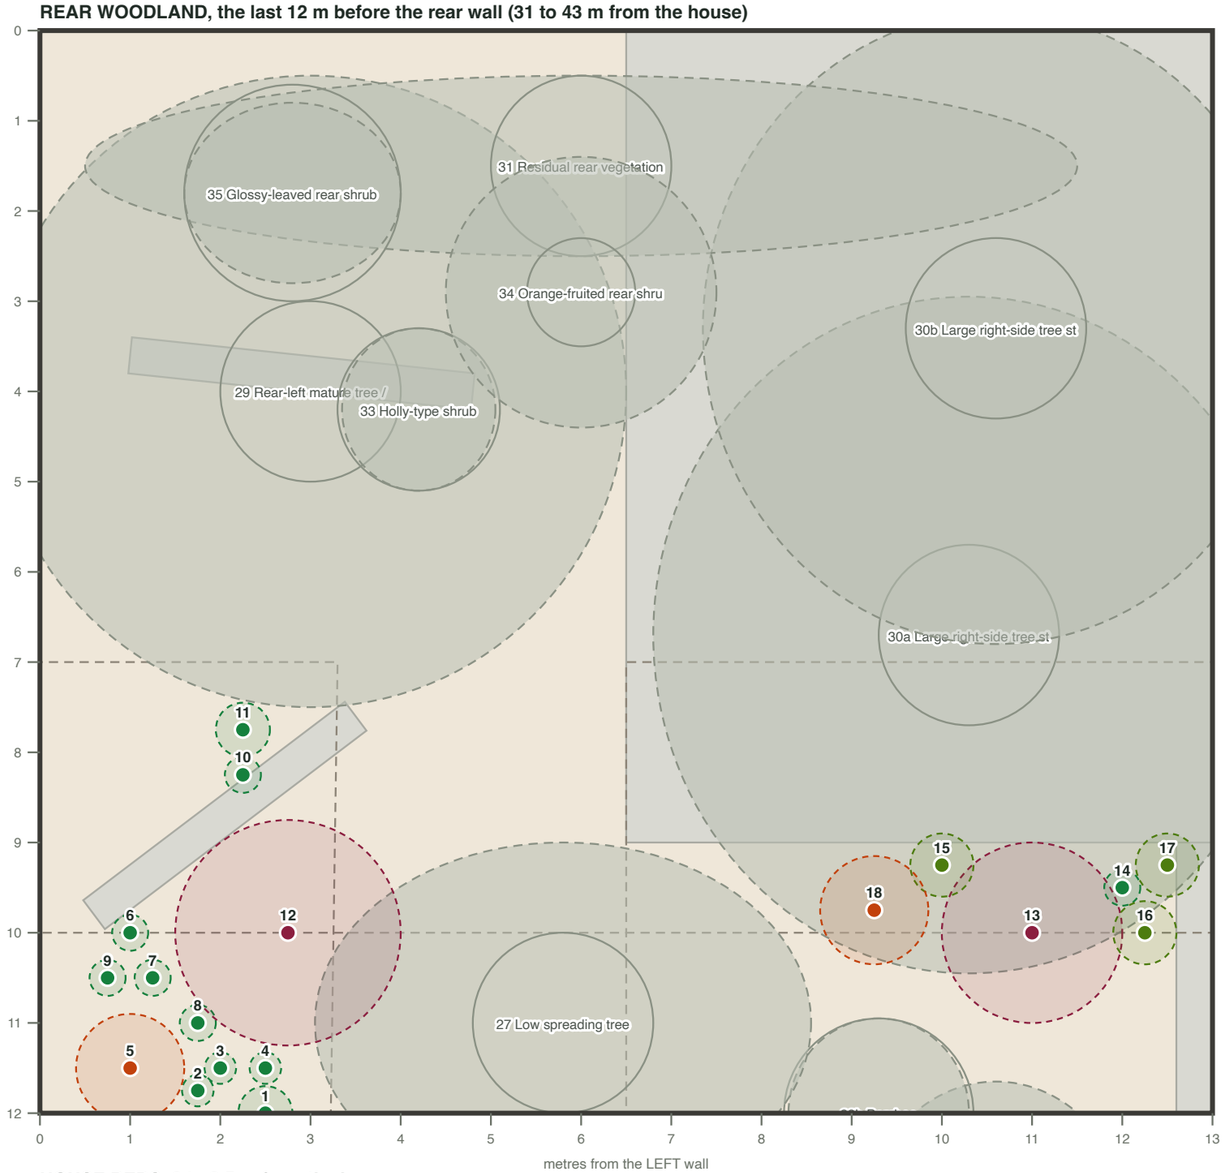

HOUSE BEDS, 0 to 3.5 m from the house

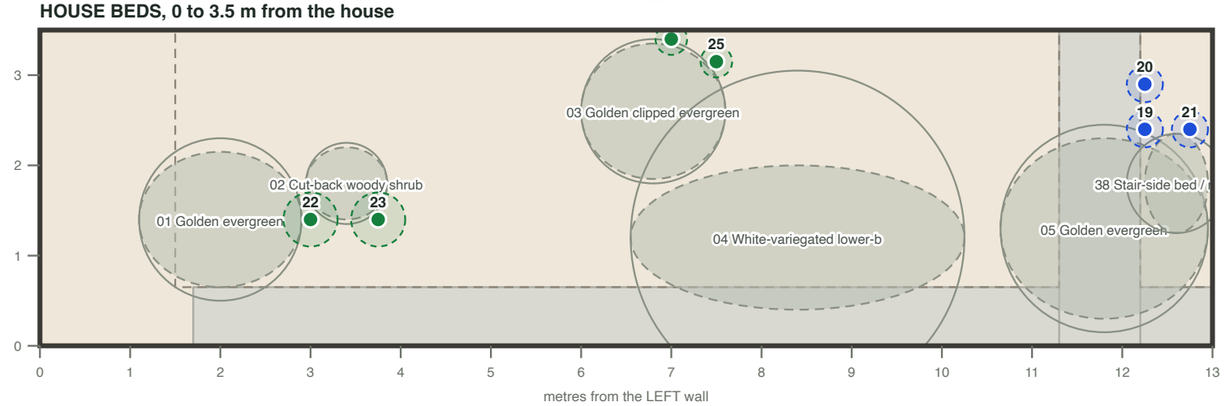

Generated 2026-11-05 from the photo survey (rev 04) and the Palmstead order of 129 plants.

SET OUT: rear pots from the REAR wall; house pots from the house; then from the left wall

1 Geranium 'Spessart'	12 from rear wall, 2.5 from left wall
2 Liriope	11.75 from rear wall, 1.75 from left wall
3 Liriope	11.5 from rear wall, 2 from left wall
4 Liriope	11.5 from rear wall, 2.5 from left wall
5 Sarcococca	11.5 from rear wall, 1 from left wall
6 Epimedium 'Sulphureum'	10 from rear wall, 1 from left wall
7 Epimedium 'Sulphureum'	10.5 from rear wall, 1.25 from left wall
8 Epimedium 'Sulphureum'	11 from rear wall, 1.75 from left wall
9 Epimedium 'Sulphureum'	10.5 from rear wall, 0.75 from left wall
10 Epimedium 'Sulphureum'	8.25 from rear wall, 2.25 from left wall
11 Geranium 'Spessart'	7.75 from rear wall, 2.25 from left wall
12 Osmanthus	10 from rear wall, 2.75 from left wall
13 Aucuba 'Crotonifolia'	10 from rear wall, 11 from left wall
14 Epimedium 'Sulphureum'	9.5 from rear wall, 12 from left wall
15 Soft shield fern	9.25 from rear wall, 10 from left wall
16 Soft shield fern	10 from rear wall, 12.25 from left wall
17 Soft shield fern	9.25 from rear wall, 12.5 from left wall
18 Sarcococca	9.75 from rear wall, 9.25 from left wall
19 Bergenia 'Bressingham White'	2.4 from house, 12.25 from left wall
20 Bergenia 'Bressingham White'	2.9 from house, 12.25 from left wall
21 Bergenia 'Bressingham White'	2.4 from house, 12.75 from left wall
22 Geranium 'Spessart'	1.4 from house, 3 from left wall
23 Geranium 'Spessart'	1.4 from house, 3.75 from left wall
24 Liriope	3.4 from house, 7 from left wall
25 Liriope	3.15 from house, 7.5 from left wall

REAR RIGHT, BEHIND THE BAMBOO

There is a hedge and a path there that are not on this plan.
Keep the path clear. Plant only in hand-diggable soil between roots.

BEFORE YOU DIG

Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.

Count check and open decisions

Check the delivery against this list before setting out.

COUNT CHECK BY VARIETY

Plant	Ordered	On plan	Pot
Anemone × hybrida 'Honorine Jobert'	3	3	2 L
Artemisia 'Powis Castle'	3	3	2 L
Aucuba japonica 'Crotonifolia'	2	2	10 L
Bergenia 'Bressingham White'	5	5	2 L
Calamagrostis brachytricha	5	5	2 L
Chaenomeles × superba 'Crimson & Gold'	2	2	2 L
Choisya ternata	1	1	7.5 L
Cotinus coggygria 'Royal Purple'	1	1	25 L
Deutzia gracilis 'Nikko'	9	9	2 L
Epimedium × versicolor 'Sulphureum'	16	16	2 L
Euphorbia amygdaloides 'Purpurea'	5	5	2 L
Geranium 'Rozanne'	6	6	2 L
Geranium macrorrhizum 'Spessart'	37	37	2 L
Liriope muscari	5	5	2 L
Nepeta racemosa 'Walker's Low'	6	6	2 L
Osmanthus × burkwoodii	1	1	5 L
Philadelphus 'Virginal'	1	1	25 L
Salvia nemorosa 'Caradonna'	5	5	2 L
Sarcococca confusa	3	3	4 L
Skimmia japonica 'Rubella'	3	3	2 L
Polystichum setiferum	5	5	2 L
Spiraea japonica 'Goldflame'	3	3	1.5 L
Viburnum × bodnantense 'Dawn'	1	1	10 L
Viburnum tinus 'Eve Price'	1	1	2 L
Total	**129**	**129**	

POTS PER BED

left border	69
right border	46
rear woodland	7
house bed, left of the stairs	4
rosemary stair bed	3

DECISIONS STILL OPEN

A06-1 Sarcococca moved 10.78 m along the bed to find part-or-shade; confirm or override.

G04-2 Skimmia 'Rubella' moved 16.1 m along the bed to find part-or-shade; confirm or override.

G04-3 Skimmia 'Rubella' moved 16.76 m along the bed to find part-or-shade; confirm or override.

K01-1 Aucuba 'Crotonifolia' at (11, 33) is in the pocket behind the bamboo; the hedge and the path there are not on the survey, keep the path clear.

K02-1 Epimedium 'Sulphureum' at (12, 33.5) is in the pocket behind the bamboo; the hedge and the path there are not on the survey, keep the path clear.

K03-1 Soft shield fern at (10, 33.75) is in the pocket behind the bamboo; the hedge and the path there are not on the survey, keep the path clear.

K03-2 Soft shield fern at (12.25, 33) is in the pocket behind the bamboo; the hedge and the path there are not on the survey, keep the path clear.

K03-3 Soft shield fern at (12.5, 33.75) is in the pocket behind the bamboo; the hedge and the path there are not on the survey, keep the path clear.

K04-1 Sarcococca at (9.25, 33.25) is in the pocket behind the bamboo; the hedge and the path there are not on the survey, keep the path clear.

WHAT THE PLAN ASSUMES

The garden is 43 by 13 m, from the estate agent plan, not measured.
Bed edges, the path and every existing plant come from a photo survey (revision 04, 24 October 2026).
The rosemary bed and its stairs are at the right-hand end of the house frontage, facing out.
Shrubs are planned at their pruned size, and may lean over the lawn but not the path.
Sun plants are only placed where nothing shades them; shade plants are never placed in open sun.
Every plant from the Palmstead order is on the plan once. There are no substitutions.

BEFORE YOU DIG

Positions come from a photo survey, not a measured one.
Set out every pot, walk the beds, then dig.

Generated 2026-11-05 from the photo survey (rev 04) and the Palmstead order of 129 plants.
